

Neighborhood Project Update

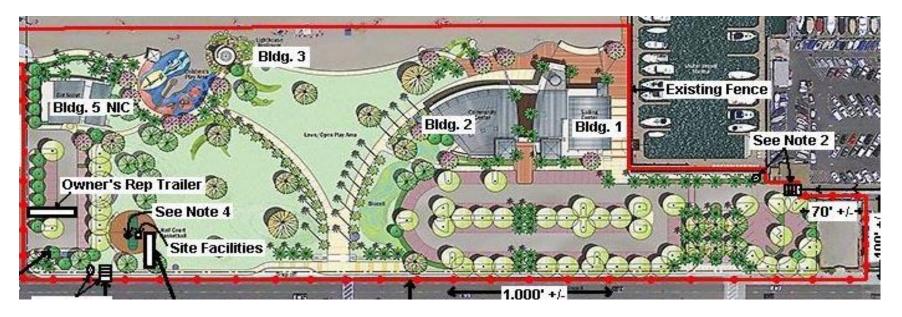


Key Dates and Milestones:

- Relocation of Fencing, Parking Closure at North Side, W. Balboa Blvd: September 3rd
- Demolition of Sidewalk at North Side, W. Balboa Blvd: September 11th thru September 19th
- New Sidewalk at North Side, W. Balboa Blvd: September 22nd thru October 31st
- Anticipated Restoration of Parking at W. Balboa Blvd: November 1, 2014

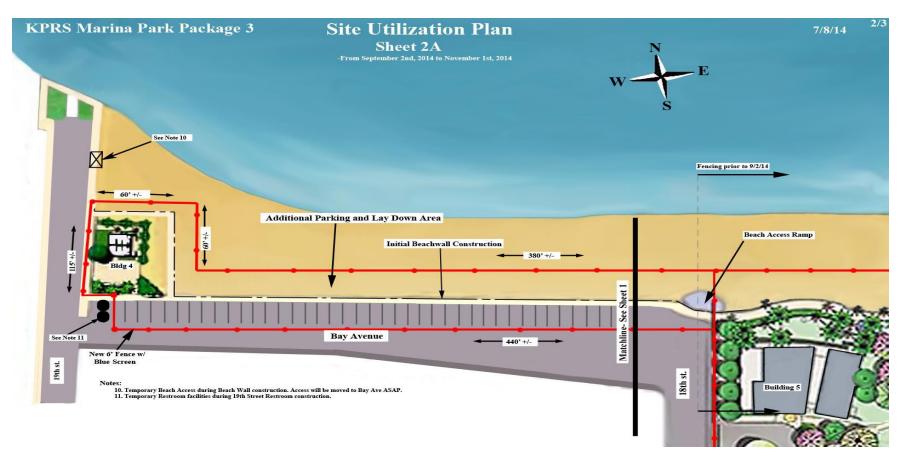


Key Dates and Milestones: PHASE 1

- Fencing at W. Bay Ave and 19th St. restroom: **September 2**nd
- Relocation of Palm Trees at 19th St. restroom: September 3rd thru September 5th
- Demolition of Restroom, Sidewalk, and Beach Wall at W. Bay Ave: September 8th thru September 19th
- New Sidewalk and Beach Wall at W. Bay Ave: September 22nd thru October 31st
- Completion of W. Bay Ave Work Phase 1: November 1, 2014

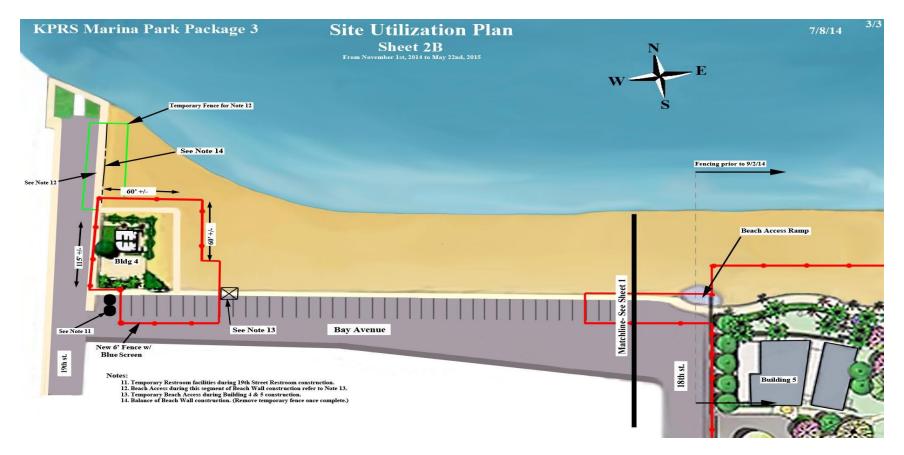

Key Dates and Milestones: Phase 2

- Demolition of 19th St. Beach Wall: **November 3rd thru November 7th**
- New 19th St. Beach Wall Construction: November 7th thru December 31st
- Restroom and Landscape Completion: May 22nd, 2015

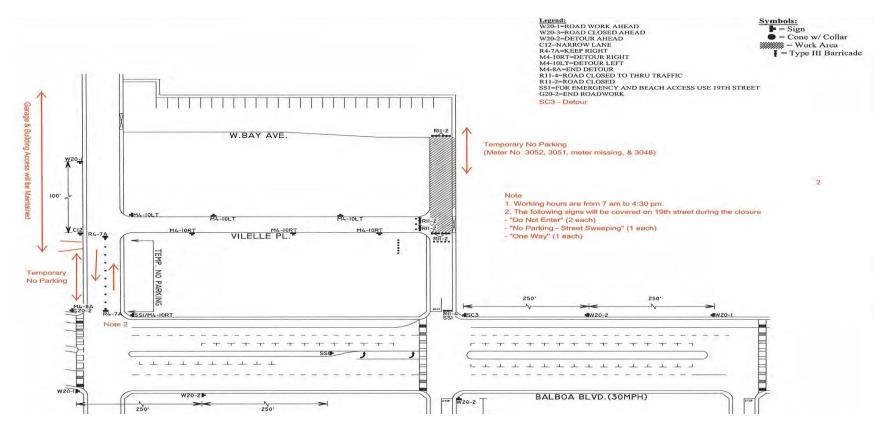

Key Dates and Milestones: 18th St and 19th St.

- Utilities work at 18th St. (traffic detour): September 2nd thru October 31st
- Temporary Water Shut Down: Sometime in the 2 Weeks of September 15th thru September 26th
 - o City provide notifications to residents prior to shut down
 - Shut down will occur during off peak hours
- Utilities work in the Alley and 15th St: **September thru November**

Stay Informed!

Sign Up to receive Marina Park project updates at:

http://www.newportbeachca.gov/index.aspx?page=108

Thank You!
