


# Rhine Channel Construction Phase Plan



# Preliminary Construction Schedule

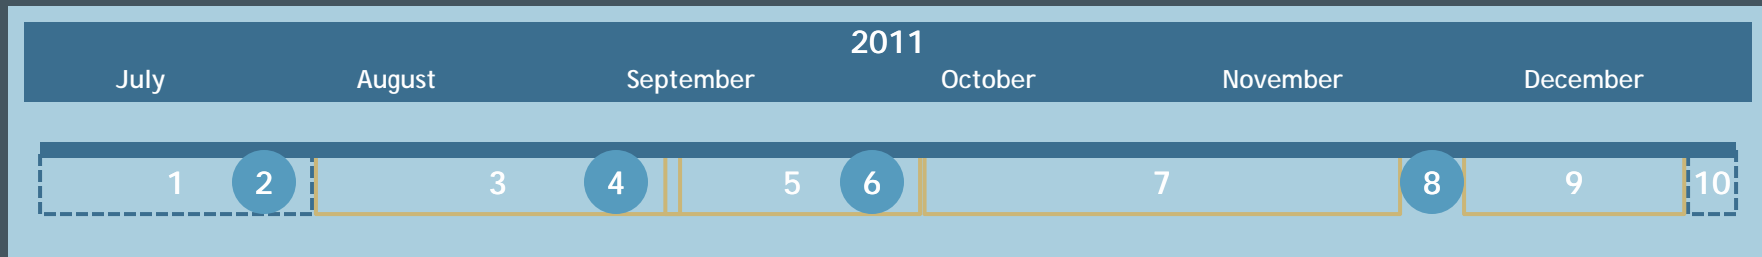

- 1. Contractor mobilization (7/1 to 7/31)*
- 2. Phase 1 slips vacated by 7/25*
- 3. Phase 1 - dredging and pile replacement (8/1 to 9/8)*
- 4. Phase 2 slips vacated by 9/5*
- 5. Phase 2 - dredging and pile replacement (9/6 to 10/5)*
- 6. Phase 3 slips vacated by 9/28*
- 7. Phase 3 - dredging and pile replacement (10/6 to 11/22)*
- 8. Phase 4 slips vacated by 12/1 (American Legion)*
- 9. Phase 4 - dredging and pile replacement (American Legion) (12/2 to 12/23)*
- 10. Contractor demobilization (12/28 to 12/30)*
