


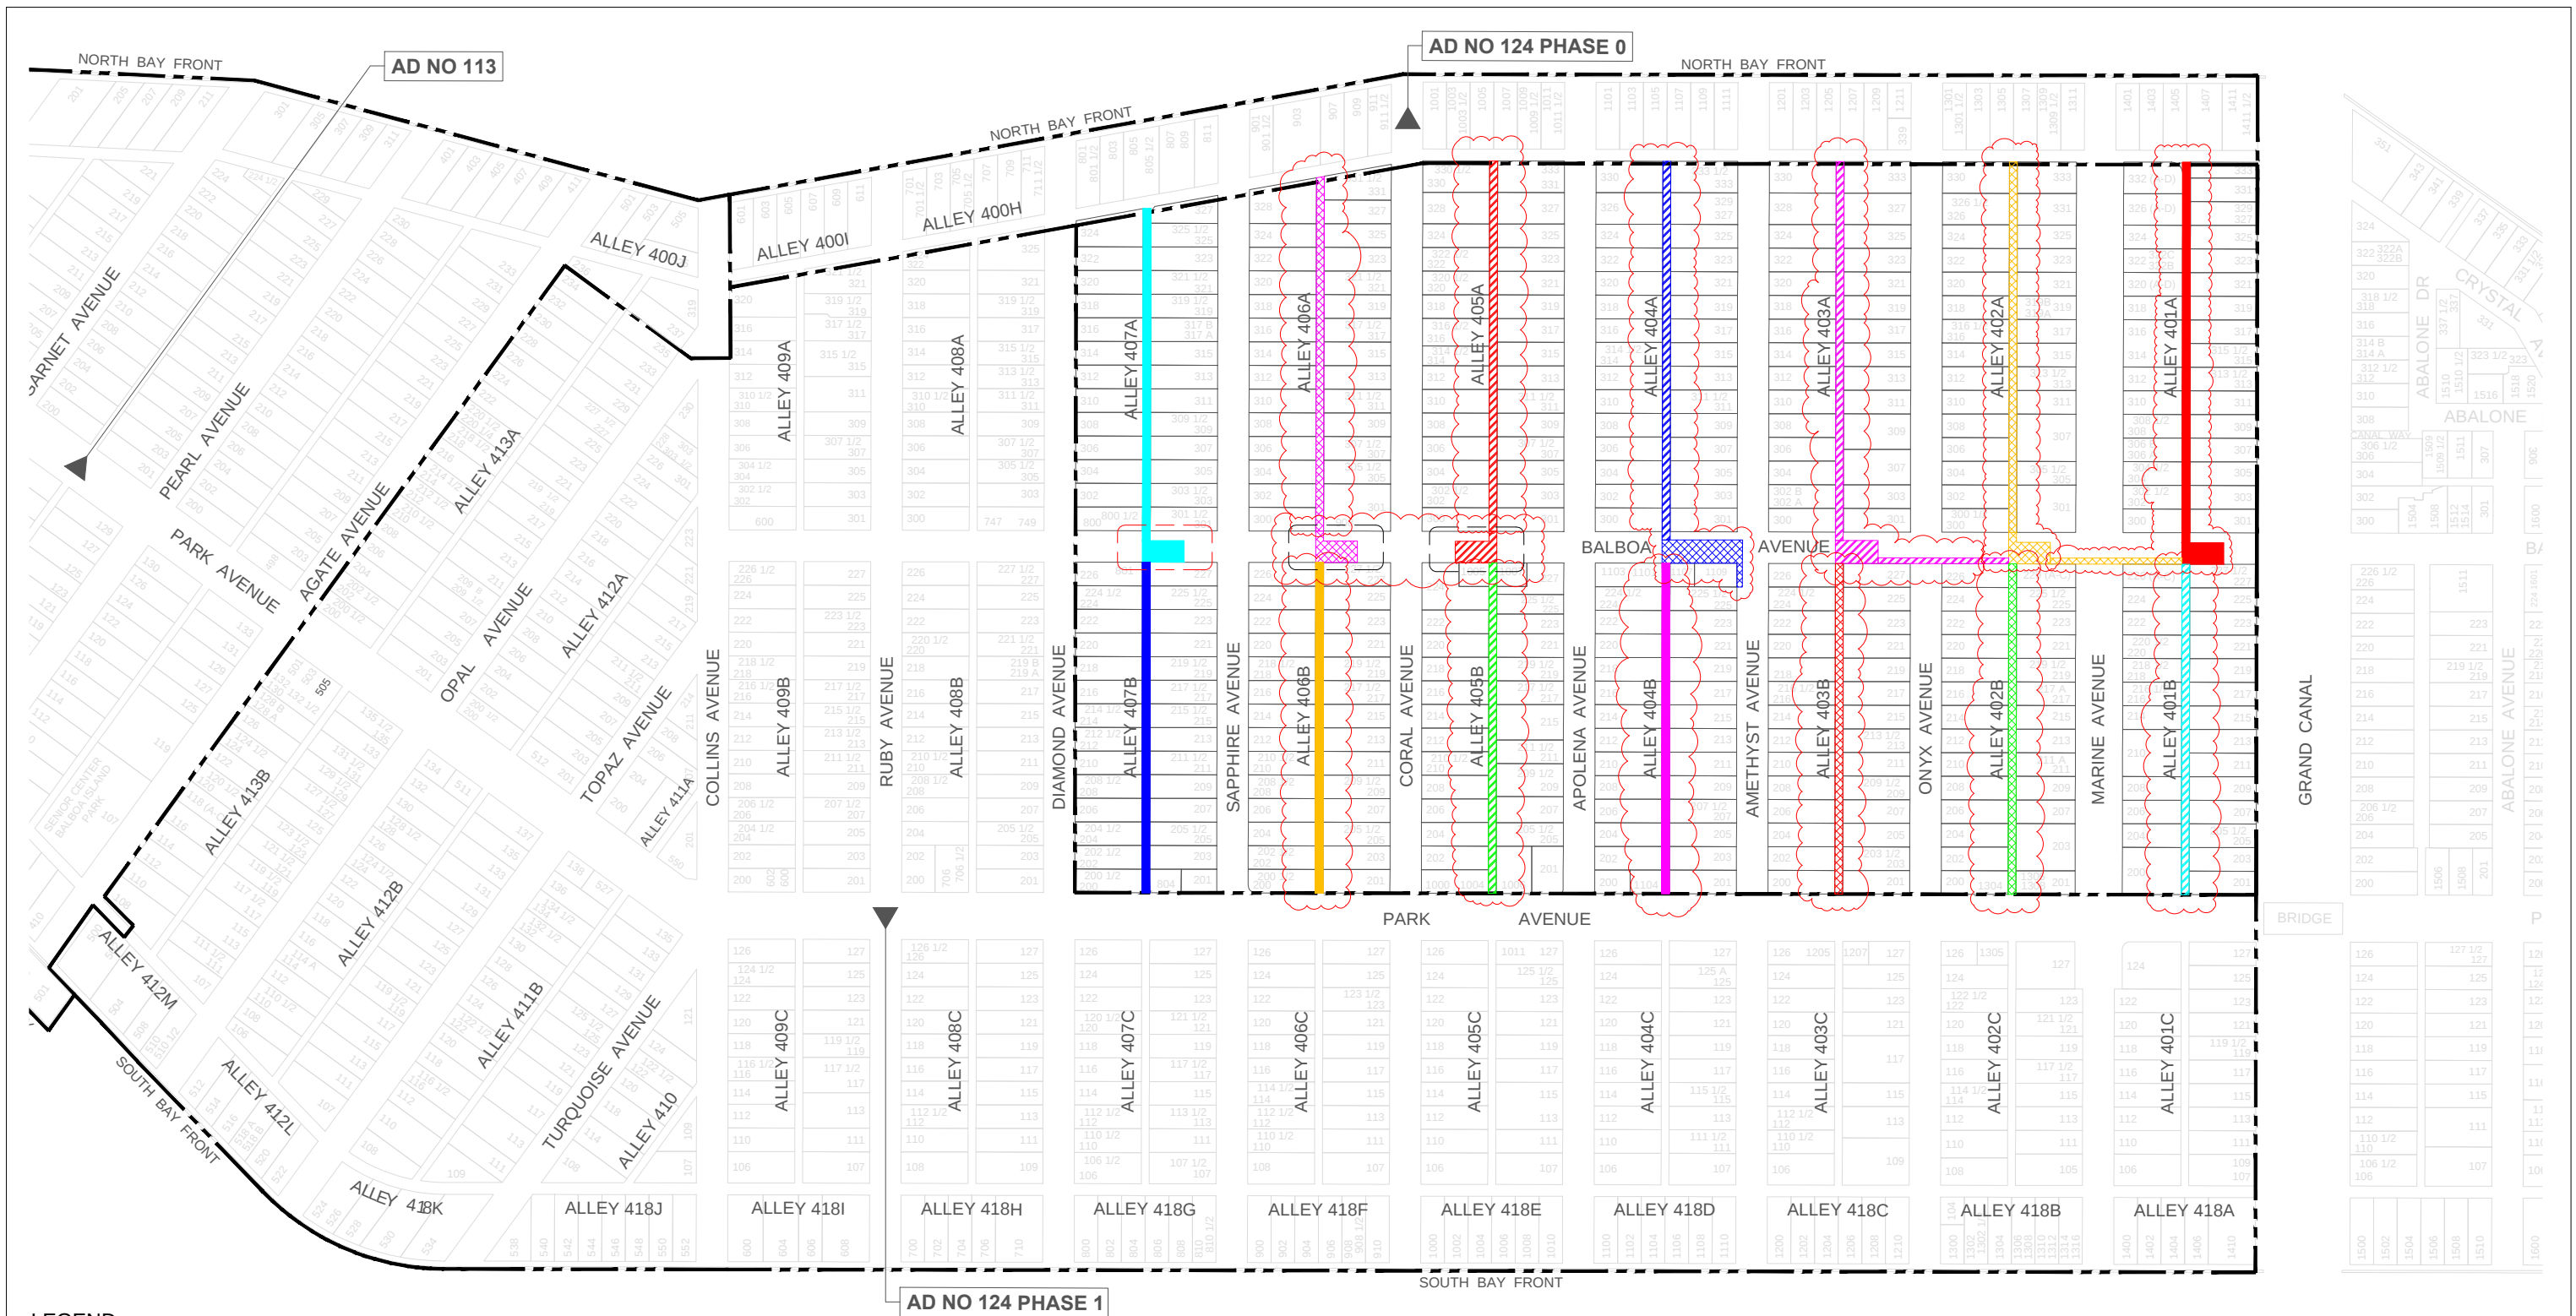

LEGEND

- PHASE 1: 02/03/25 - 03/21/25
- PHASE 2: 03/24/25 - 05/02/25
- PHASE 3: 04/14/25 - 05/23/25
- PHASE 4: 04/23/25 - 05/16/25
- PHASE 5: 05/05/25 - 06/20/25
- PHASE 6: 05/05/25 - 06/20/25
- PHASE 7: 06/23/25 - 07/30/25
- PHASE 8: 06/23/25 - 07/30/25
- PHASE 9: 07/28/25 - 09/05/25
- PHASE 10: 07/28/25 - 09/05/25
- PHASE 11: 09/04/25 - 10/07/25
- PHASE 12: 09/08/25 - 10/08/25
- PHASE 13: 10/08/25 - 11/21/25
- PHASE 14: 12/01/25 - 01/16/26
- PHASE 15: 01/20/26 - 02/27/26
- ASSESSMENT DISTRICT AREA BOUNDARY
- COMPLETED WORK

VAULT WORK

 10/09/25 - 11/20/25

VAULT WORK

 11/20/25 - 12/02/25

\*\*PHASING PLAN SUBJECT TO CHANGE

|                                                                                      |  |                                                  |        |
|--------------------------------------------------------------------------------------|--|--------------------------------------------------|--------|
| UNDERGROUND UTILITY ASSESSMENT DISTRICT<br>NO. 124 (CENTRAL BALBOA ISLAND - PHASE 2) |  | CITY OF NEWPORT BEACH<br>PUBLIC WORKS DEPARTMENT |        |
| PHASING PLAN                                                                         |  | C-9451-2                                         | 1/7/26 |
