
Manager's Report

October 10, 2012

Harbor Resources





 Lower Newport Bay Dredging Project
Phases I & II

 1 - 2 Weeks Projected Schedule

 Active Dredge Area

 Dredging Complete

For more information contact Harbor Resources Manager,
Chris Miller: (949) 644-3043
cmiller@newportbeachca.gov




CurrentDredgingUpdateFigure11 Updated: 10/10/2012

Linda Isle - Backside



Linda Isle – Backside

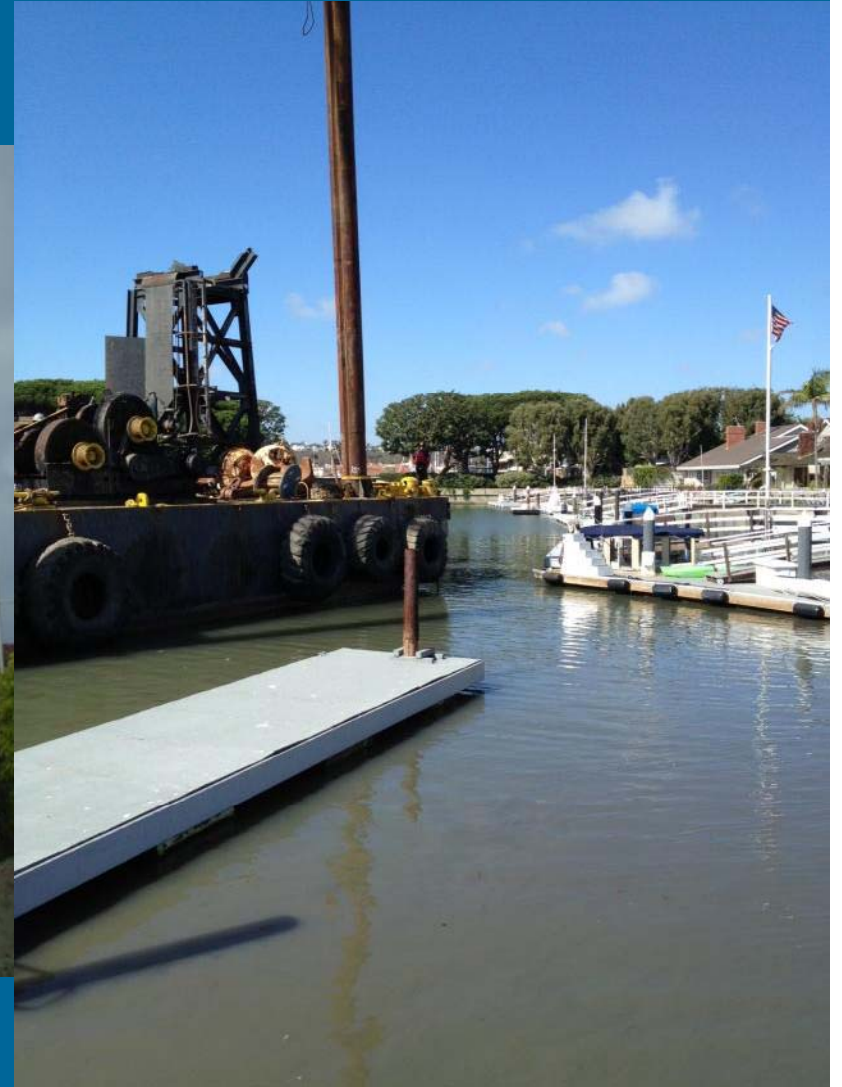

Linda Isle - Backside



Other Issues

- New pump-outs coming to Newport soon
 - Grant paperwork is in the final stages of approval
 - Hoping to replace all of the City's pump-out stations (5) with new, larger and stronger machines.
 - State pays 75% of the cost
 - City pays 25% of cost

Regional General Permit - Status

- Coastal Commission hearing October 11
- Corp permit is expected mid-November

Other Issues

- Tidelands Management Committee
 - October Meeting – **CANCELLED**

Next Meeting

November 14, 2012
6:00 PM

For More Information

- <http://www.newportbeachca.gov/HarborResources>
- *Chris Miller, Harbor Resources Manager*
 - cmiller@newportbeachca.gov
 - (949) 644-3043
- *Shannon Levin, Harbor Resources Supervisor*
 - shannon@newportbeachca.gov
 - (949) 644-3041
