Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
3455	Procure Partitions	35	29-Jan-14	20-Mar-14			130
Mobilization		180	13-Jan-14	24-Sep-14			0
1005	Mobilization	0	13-Jan-14				0
1200	Mobilize Equipments	3	13-Jan-14	15-Jan-14			0
1210	Mobilize Trailer	3	13-Jan-14	15-Jan-14			0
1220	Topo Site	3	13-Jan-14	15-Jan-14			0
1230	Pre-Soak Site	1	16-Jan-14	16-Jan-14			0
1240	Implement SWPPP	180	13-Jan-14	24-Sep-14			0
Clear and Grub/ Demolition		5	17-Jan-14	24-Jan-14			0
1010	Clear and Grub/ Demolition	0	17-Jan-14				0
1250	Clear and Grub Site	2	17-Jan-14	21-Jan-14			0
1260	Demo Site	3	22-Jan-14	24-Jan-14			0
Earthwork		26	27-Jan-14	05-Mar-14			65
1020	Earthwork	0	27-Jan-14				0
1270	Export Unsuitable Material	10	27-Jan-14	10-Feb-14			0
1275	Excess Export Dirt Testing	10	11-Feb-14	25-Feb-14			68
1280	Cut & Fill Site	12	11-Feb-14	27-Feb-14			0
1290	Fine Grade Building Pad	1	28-Feb-14	28-Feb-14			65
1300	Export Excess Material	3	03-Mar-14	05-Mar-14			65
Sewer Construction		4	28-Feb-14	05-Mar-14			69
1030	Sewer Construction	0	28-Feb-14				66
1310	Install 6" VCP Sewer/ Connect	2	28-Feb-14	03-Mar-14			69
1320	Modify Existing Manhole	2	04-Mar-14	05-Mar-14			69
Storm Drain Construction		26	04-Mar-14	08-Apr-14			69
1040	Storm Drain Construction	0	04-Mar-14				69
1330	Install RCP Storm Drain	15	04-Mar-14	24-Mar-14			69
1340	Install Manhole	6	25-Mar-14	01-Apr-14			69
1350	Install CDS Unit	5	02-Apr-14	08-Apr-14			69
Infiltration System		9	09-Apr-14	21-Apr-14			69
1050	Infiltration System	0	09-Apr-14				69
1360	Excavate for System	3	09-Apr-14	11-Apr-14			69
1370	Place Fabric	1	14-Apr-14	14-Apr-14			69

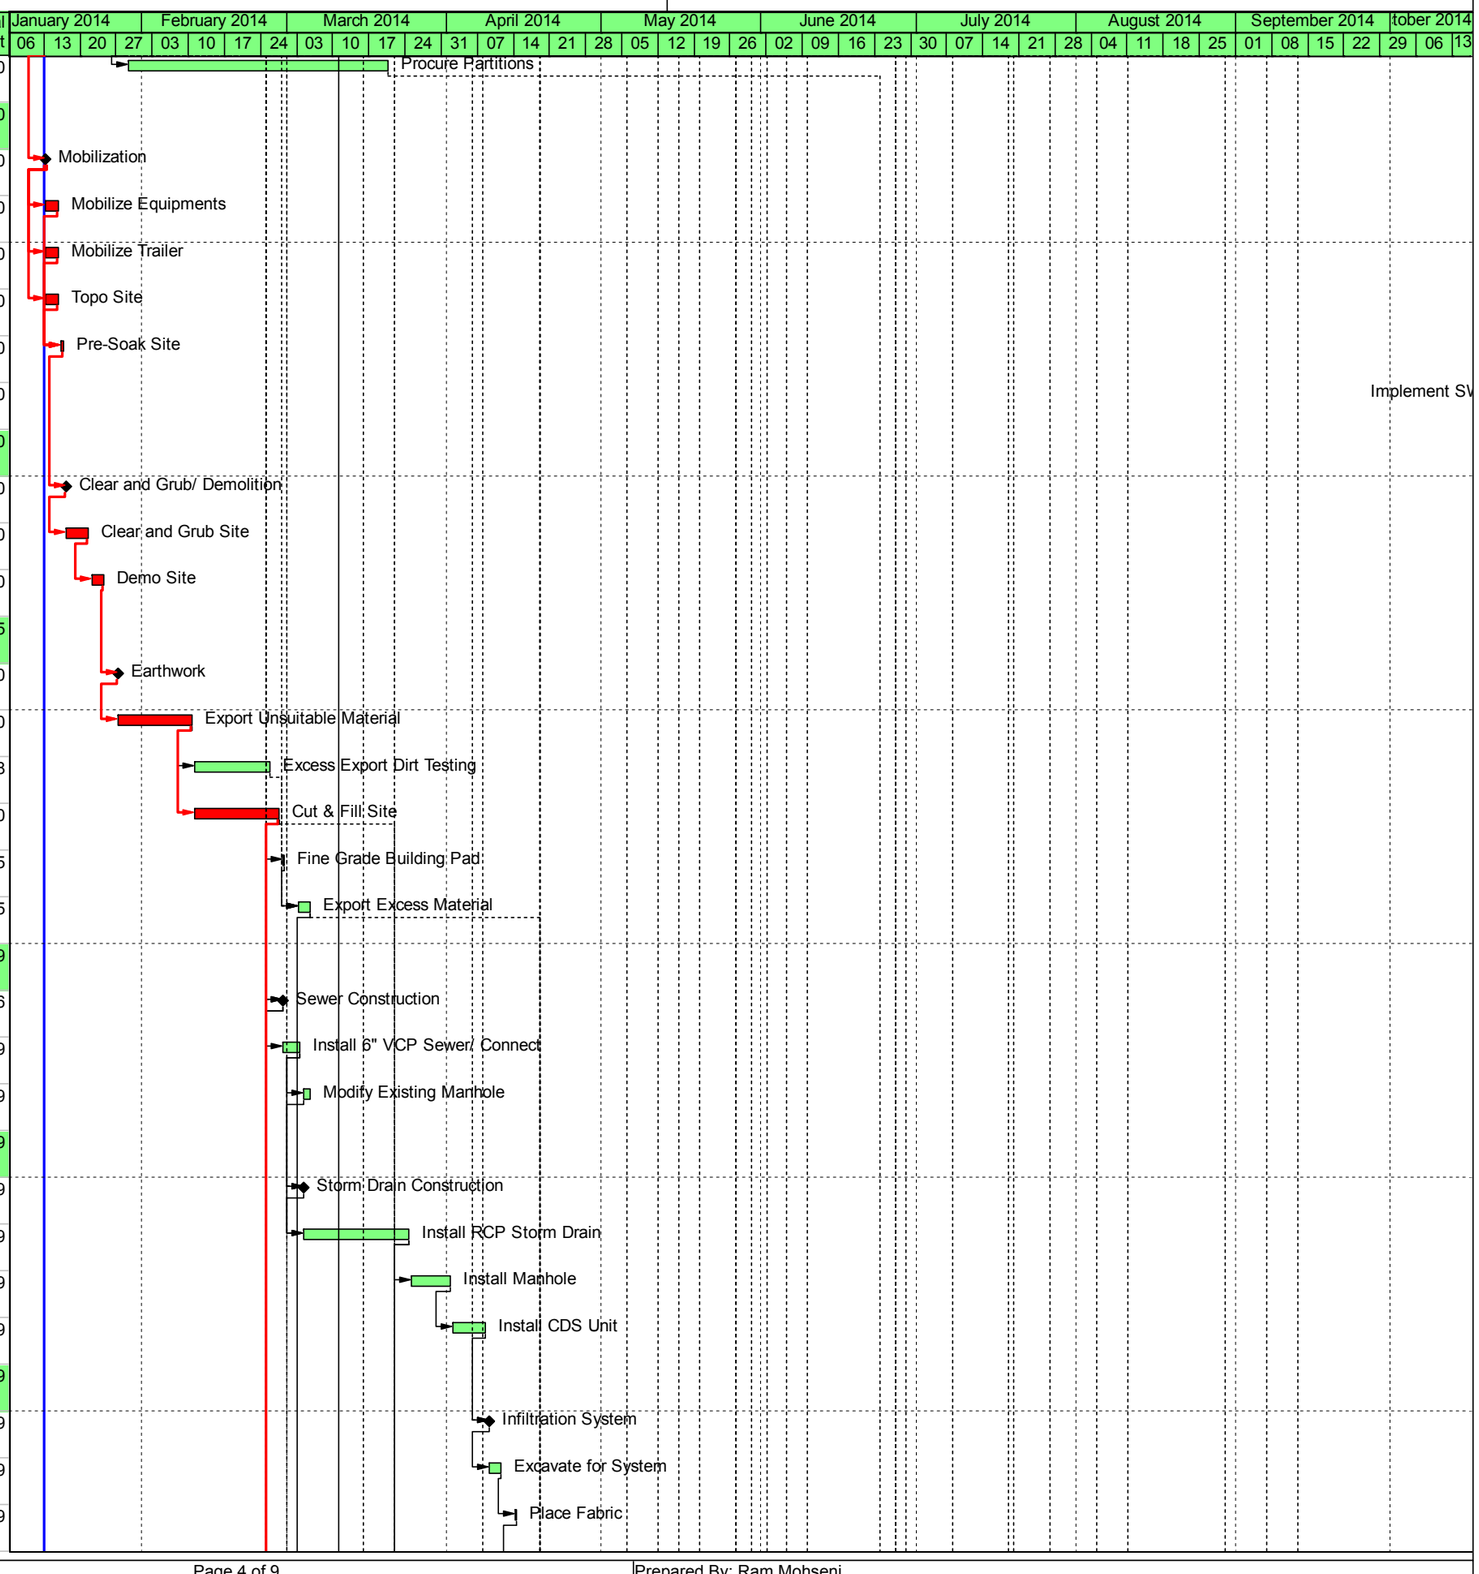

© Primavera Systems, Inc.

Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
1380	Install Rock	1	15-Apr-14	15-Apr-14			69
1390	Install Infiltration System	1	16-Apr-14	16-Apr-14			69
1400	Make Connection	1	17-Apr-14	17-Apr-14			69
1410	Backfill Vault	2	18-Apr-14	21-Apr-14			69
Area Drain System		32	25-Mar-14	07-May-14			69
1060	Area Drain System	0	25-Mar-14				69
1420	Install PVC Drain pipe	20	25-Mar-14	21-Apr-14			69
1430	Install Catch Basins	12	22-Apr-14	07-May-14			69
Domestic Water Construction		9	28-Feb-14	12-Mar-14			66
1070	Domestic Water Construction	0	28-Feb-14				66
1440	Hot Top to Existing Line	1	28-Feb-14	28-Feb-14			66
1450	Install PVC Water Lines	3	03-Mar-14	05-Mar-14			66
1460	Install Copper Waterlines	5	06-Mar-14	12-Mar-14			66
Concrete/ Masonary Construc		86	28-Feb-14	27-Jun-14			20
1080	Concrete/ Masonary Construction	0	22-Apr-14				69
1470	Install Verdura Wall	10	28-Feb-14	13-Mar-14			76
1480	Install Grand Stairway Footing	2	28-Feb-14	03-Mar-14			0
1490	Install Grand Stairway Check Wall	5	04-Mar-14	10-Mar-14			64
1500	Install Grand Stairway Landing	5	11-Mar-14	17-Mar-14			64
1510	Install Concrete Stairs Behind Backstop	5	18-Mar-14	24-Mar-14			64
1520	Install Ballfield Seat Wall	5	25-Mar-14	31-Mar-14			64
1530	Install Footing for Sound Wall @ Superior	3	28-Feb-14	04-Mar-14			0
1540	Install Block Sound Wall @ Superior	4	05-Mar-14	10-Mar-14			0
1550	Install Architectural Bladewall Footing	3	05-Mar-14	07-Mar-14			1
1560	Install Architectural Bladewall	3	11-Mar-14	13-Mar-14			0
1570	Install Retaining Wall Footing @ Tot Lot	4	05-Mar-14	10-Mar-14			3
1580	Install Retaining Wall @ Tot-Lot	5	14-Mar-14	20-Mar-14			0
1590	Install Turf Stairs @ Tot-Lot	4	21-Mar-14	26-Mar-14			0
1600	Install Footing Retaining Wall W/Cable Railing	3	27-Mar-14	31-Mar-14			0
1610	Install Retaining Wall W/ Cable Railing	3	01-Apr-14	03-Apr-14			0
1620	Install Butterfly Garden Seat Wall	3	04-Apr-14	08-Apr-14			0
1630	Install Over Look Trellis Seat Wall	7	09-Apr-14	17-Apr-14			0

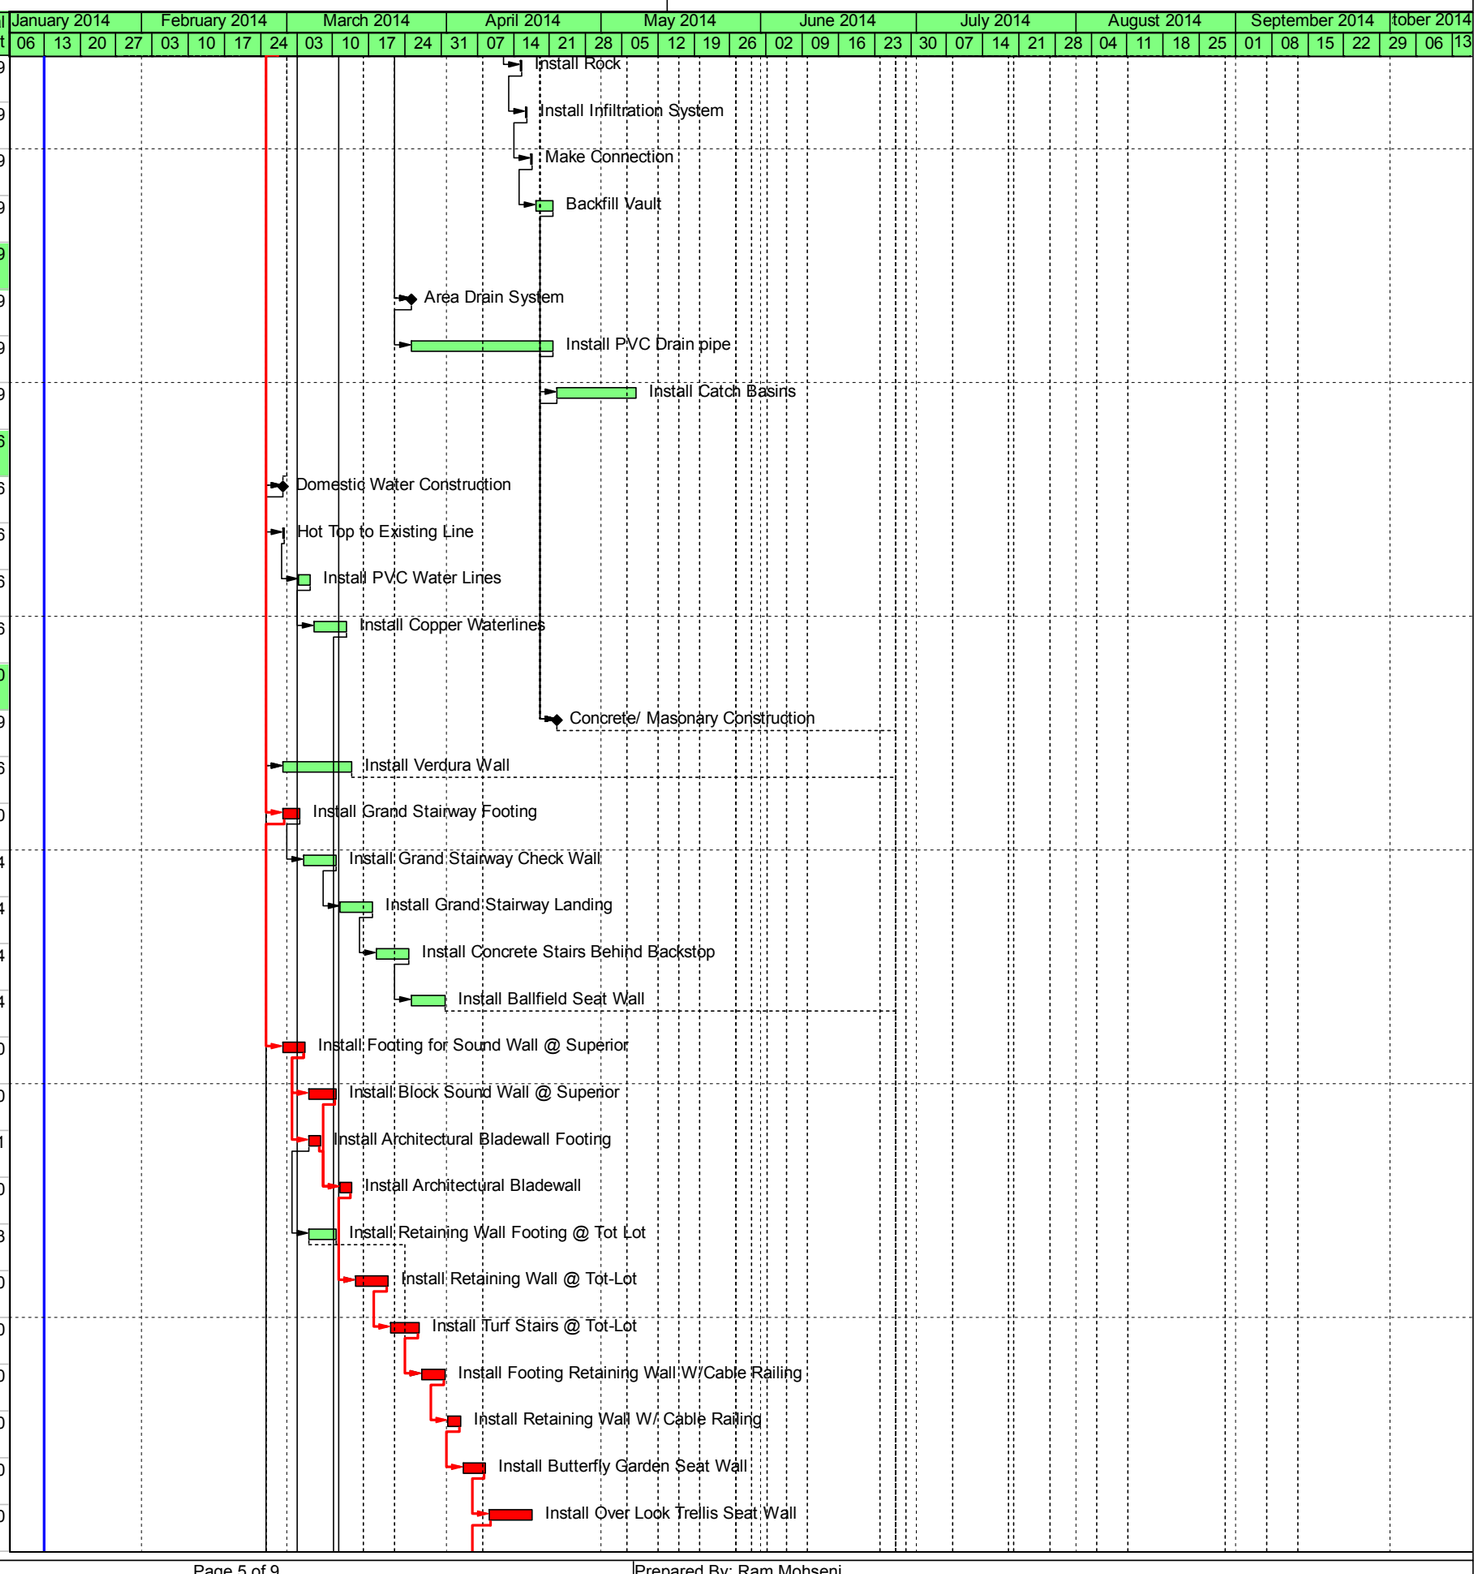

© Primavera Systems, Inc.

Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
1640	Install Monument Sign Footing	3	09-Apr-14	11-Apr-14			0
1650	Install Monument Sign	4	14-Apr-14	17-Apr-14			0
1660	Install Bridge Wall Footing	3	18-Apr-14	22-Apr-14			0
1670	Install Bridge Wall	4	23-Apr-14	28-Apr-14			0
1680	Install V-Gutter	5	29-Apr-14	05-May-14			0
1690	Install Buterfly Garden Header	4	06-May-14	09-May-14			0
1700	Install Butterfly Garden Subslab	4	12-May-14	15-May-14			0
1710	Install Butterfly Garden Flagstone Pavers	2	16-May-14	19-May-14			0
1720	Install Butterfly Garden Concrete Pavers	7	20-May-14	28-May-14			0
1730	Install Drywall under Pavers	2	29-May-14	30-May-14			0
1740	Install Concrete Header @ Vehicular Area	3	02-Jun-14	04-Jun-14			0
1750	Install Concrete Subslab @ Vehicular Area	3	05-Jun-14	09-Jun-14			0
1760	Install Concrete Pavers @ Vehicular Area	3	10-Jun-14	12-Jun-14			0
1770	Install Concrete Pavement	4	13-Jun-14	18-Jun-14			0
1780	Install Concrete Pavement w/Seaded Aggregate	10	13-Jun-14	26-Jun-14			21
1790	Install Grass Crete Pavers	3	13-Jun-14	17-Jun-14			0
1800	Install Curb @ Access Road	3	18-Jun-14	20-Jun-14			0
1810	Install Mow Curb	3	23-Jun-14	25-Jun-14			0
1820	Install Stamp Concrete @ Bridge	2	26-Jun-14	27-Jun-14			0
Misc Pavement Construction		9	30-Jun-14	10-Jul-14			20
1090	Misc Pavement Construction	0	30-Jun-14				20
1830	Install D.G Paving	2	30-Jun-14	01-Jul-14			20
1840	Install In Field Mix	2	02-Jul-14	03-Jul-14			20
1850	Install Crushed Rock @ Access Road	5	04-Jul-14	10-Jul-14			20
Electrical Construction		101	13-Mar-14	31-Jul-14			39
1100	Electrical Construction	0	13-Mar-14				66
1870	Install Conduit	20	13-Mar-14	09-Apr-14			66
1880	Install Foundations	10	10-Apr-14	23-Apr-14			66
1890	Coordinate/ Install SCE Pad	5	24-Apr-14	30-Apr-14			66
1900	Install Pull Boxes	3	04-Jul-14	08-Jul-14			20
1910	Pull Wire	2	09-Jul-14	10-Jul-14			20
2580	Install Poles/ Fixtures	10	11-Jul-14	24-Jul-14			20

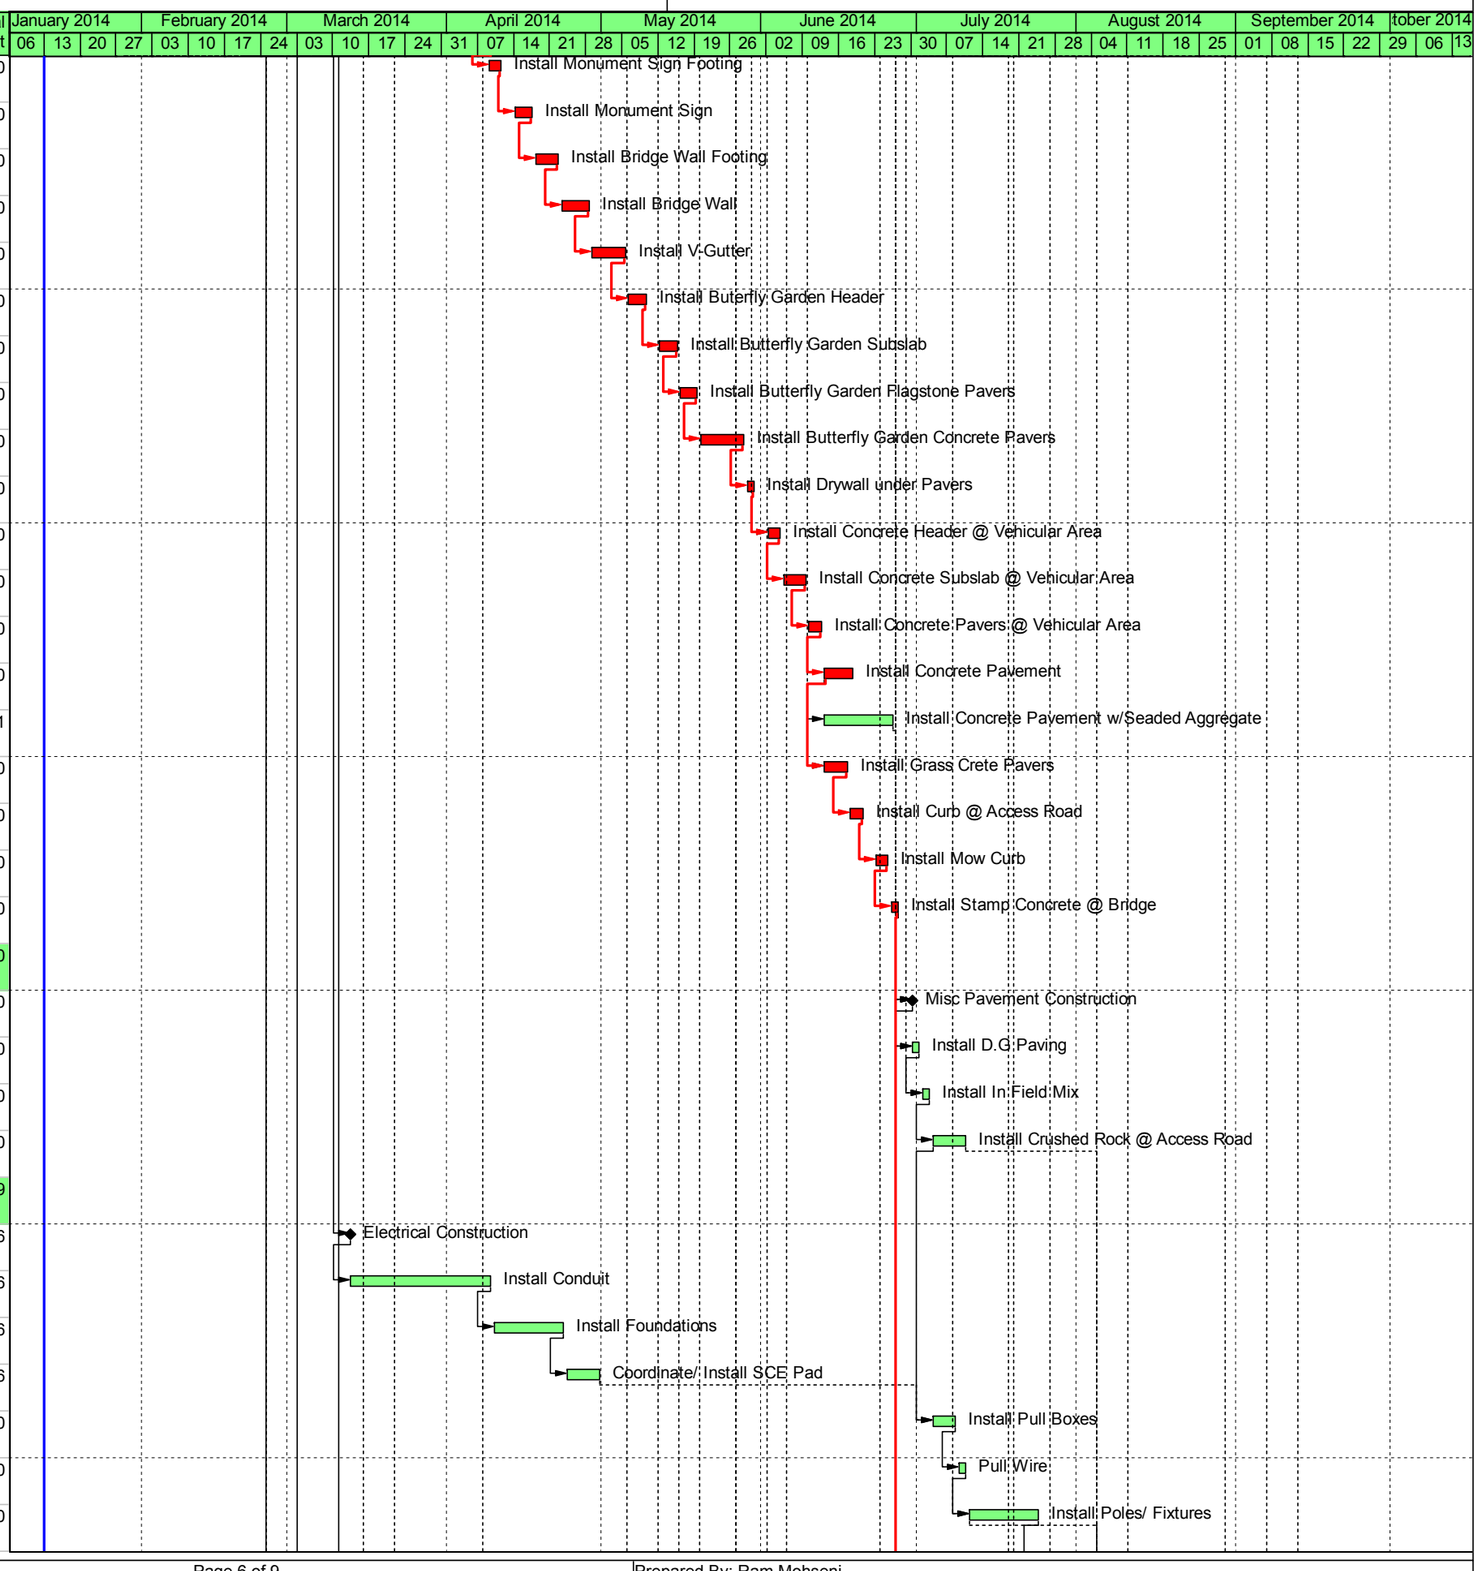

© Primavera Systems, Inc.

Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
2590	Electrical Clean up/ Punch List	5	25-Jul-14	31-Jul-14			39
Fence Construction		29	30-Jun-14	07-Aug-14			0
1110	Fence Construction	0	30-Jun-14				0
1190	Install Fence Concrete Footing & Posts	7	30-Jun-14	08-Jul-14			0
2600	Install Perimeter Chain Link Fence W/ Barbed Wires	9	09-Jul-14	21-Jul-14			0
2620	Install Chain Link Gates	4	22-Jul-14	25-Jul-14			0
2630	Install Cable Rails	9	28-Jul-14	07-Aug-14			0
USA Shade Structure		59	30-Jun-14	18-Sep-14			4
1120	USA Shade Structure	0	30-Jun-14				4
1920	Shade Structure Fabrication Drawings & Material Procurement	15	30-Jun-14	18-Jul-14			4
1930	Shade Structure Foundation Install & As-built Survey	10	21-Jul-14	01-Aug-14			4
1940	As-built Review & Fabrication Drawing Refinement	5	04-Aug-14	08-Aug-14			4
1950	Fabricate Shade Structure	24	11-Aug-14	11-Sep-14			4
1960	Install Shade Structure	5	12-Sep-14	18-Sep-14			4
Play Area Construction		24	30-Jun-14	31-Jul-14			5
1130	Play Area Construction	0	30-Jun-14				5
1970	Install Play Equipment	10	30-Jun-14	11-Jul-14			5
1980	Install Concrete Pedestal	3	14-Jul-14	16-Jul-14			5
1990	Install Concrete Curb/ Sub Base	4	17-Jul-14	22-Jul-14			5
2000	Install Play Surfacing	5	23-Jul-14	29-Jul-14			5
2010	Install Fabric	1	30-Jul-14	30-Jul-14			5
2020	Install Play Sand	1	31-Jul-14	31-Jul-14			5
Irrigation Construction		74	28-Feb-14	11-Jun-14			41
1140	Irrigation Construction	0	28-Feb-14				41
2030	Install 4" POC/ Backflow	3	28-Feb-14	04-Mar-14			41
2040	Install Sleeves	4	05-Mar-14	10-Mar-14			41
2050	Install Irrigation Main/ Wires	6	11-Mar-14	18-Mar-14			41
2060	Install Valve/ Boxes	12	19-Mar-14	03-Apr-14			41
2070	Install Lateral Lines	30	04-Apr-14	15-May-14			41
2080	Install Heads	10	16-May-14	29-May-14			41
2090	Install Drip System	4	30-May-14	04-Jun-14			41
2100	Install Controllers	2	05-Jun-14	06-Jun-14			41

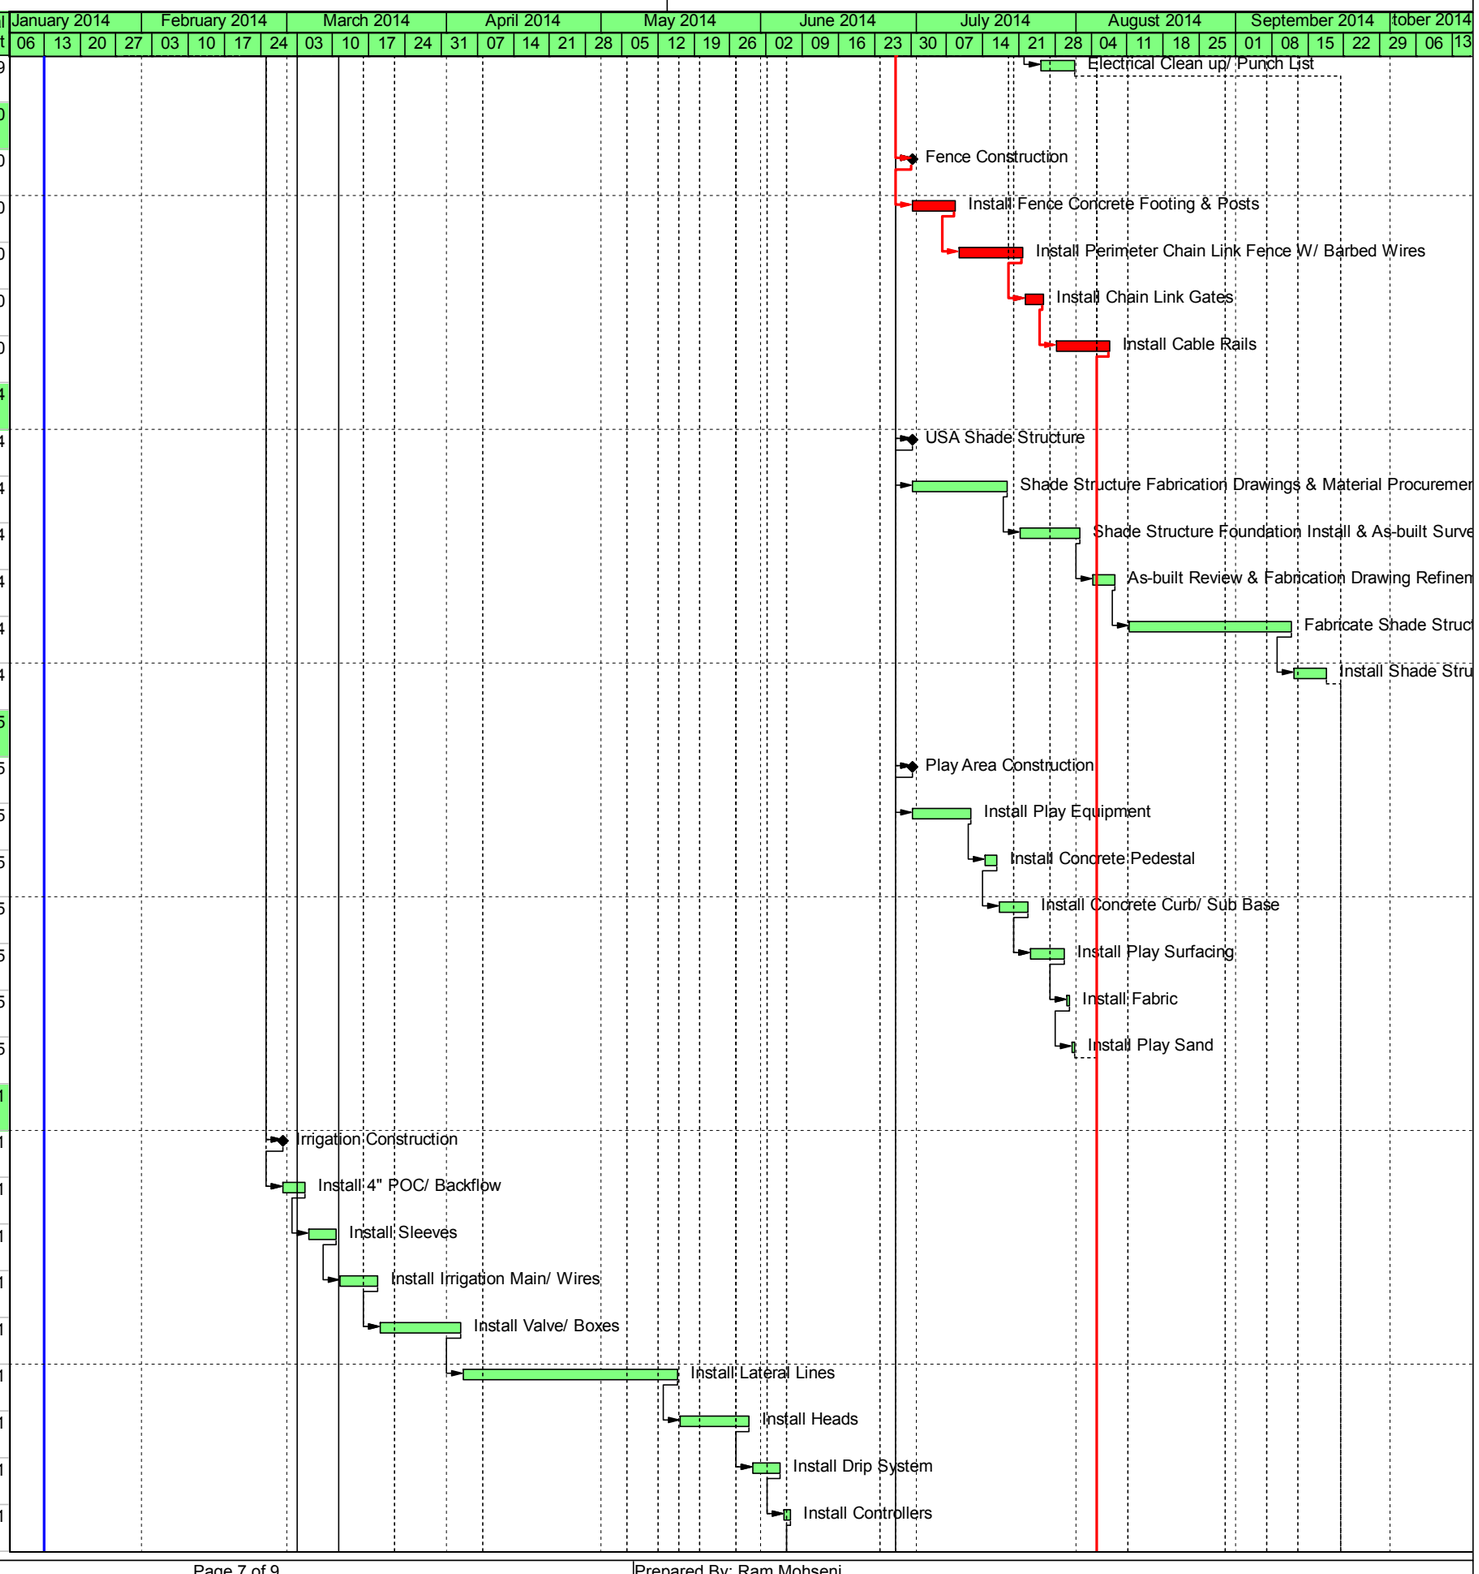

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Prepared By: Ram Mohseni

© Primavera Systems, Inc.

Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
2110	Install Booster Pump	2	09-Jun-14	10-Jun-14			41
2120	Perform Coverage Test	1	11-Jun-14	11-Jun-14			41
Planting		34	08-Aug-14	24-Sep-14			0
1150	Planting	0	08-Aug-14				0
2130	Soil Prepr Site	4	08-Aug-14	13-Aug-14			0
2140	Plant Trees	5	14-Aug-14	20-Aug-14			0
2150	Plant Shrubs	2	21-Aug-14	22-Aug-14			0
2160	Plant Ground Cover	6	25-Aug-14	01-Sep-14			0
2170	Install Landscape Boulders	2	02-Sep-14	03-Sep-14			0
2180	Fine Grade Site	2	04-Sep-14	05-Sep-14			0
2190	Hydroseed Site	2	08-Sep-14	09-Sep-14			0
2200	Install Mulch	4	10-Sep-14	15-Sep-14			0
2210	Install SOD	3	16-Sep-14	18-Sep-14			0
2220	Commence Maintenance	4	19-Sep-14	24-Sep-14			0
Site Furnishings		4	30-Jun-14	03-Jul-14			59
1160	Site Furnishings	0	30-Jun-14				58
2230	Install Drinking Fountains	2	30-Jun-14	01-Jul-14			61
2240	Install Bat Racks	1	30-Jun-14	30-Jun-14			62
2250	Install Dugout Benches	2	30-Jun-14	01-Jul-14			61
2260	Install Benches	3	30-Jun-14	02-Jul-14			60
2270	Install BBQ Grill	1	30-Jun-14	30-Jun-14			62
2280	Install Bicycle Rack	1	30-Jun-14	30-Jun-14			62
2290	Install Picnic Table	2	30-Jun-14	01-Jul-14			61
2300	Install Benches	3	30-Jun-14	02-Jul-14			60
2310	Install Waste Dispenser	2	30-Jun-14	01-Jul-14			61
2320	Install Concrete Sphere Bollards	4	30-Jun-14	03-Jul-14			59
2325	Install Precast Concrete Pedestal	2	30-Jun-14	01-Jul-14			61
2330	Install Precast Concrete Plaque Pedestals	2	30-Jun-14	01-Jul-14			61
2340	Install Habitat Signs	2	30-Jun-14	01-Jul-14			61
2350	Install Baseball Field Accessories	1	30-Jun-14	30-Jun-14			62
Building Construction		85	06-Mar-14	02-Jul-14			60
2360	Excvate for Building Footing	1	06-Mar-14	06-Mar-14			65

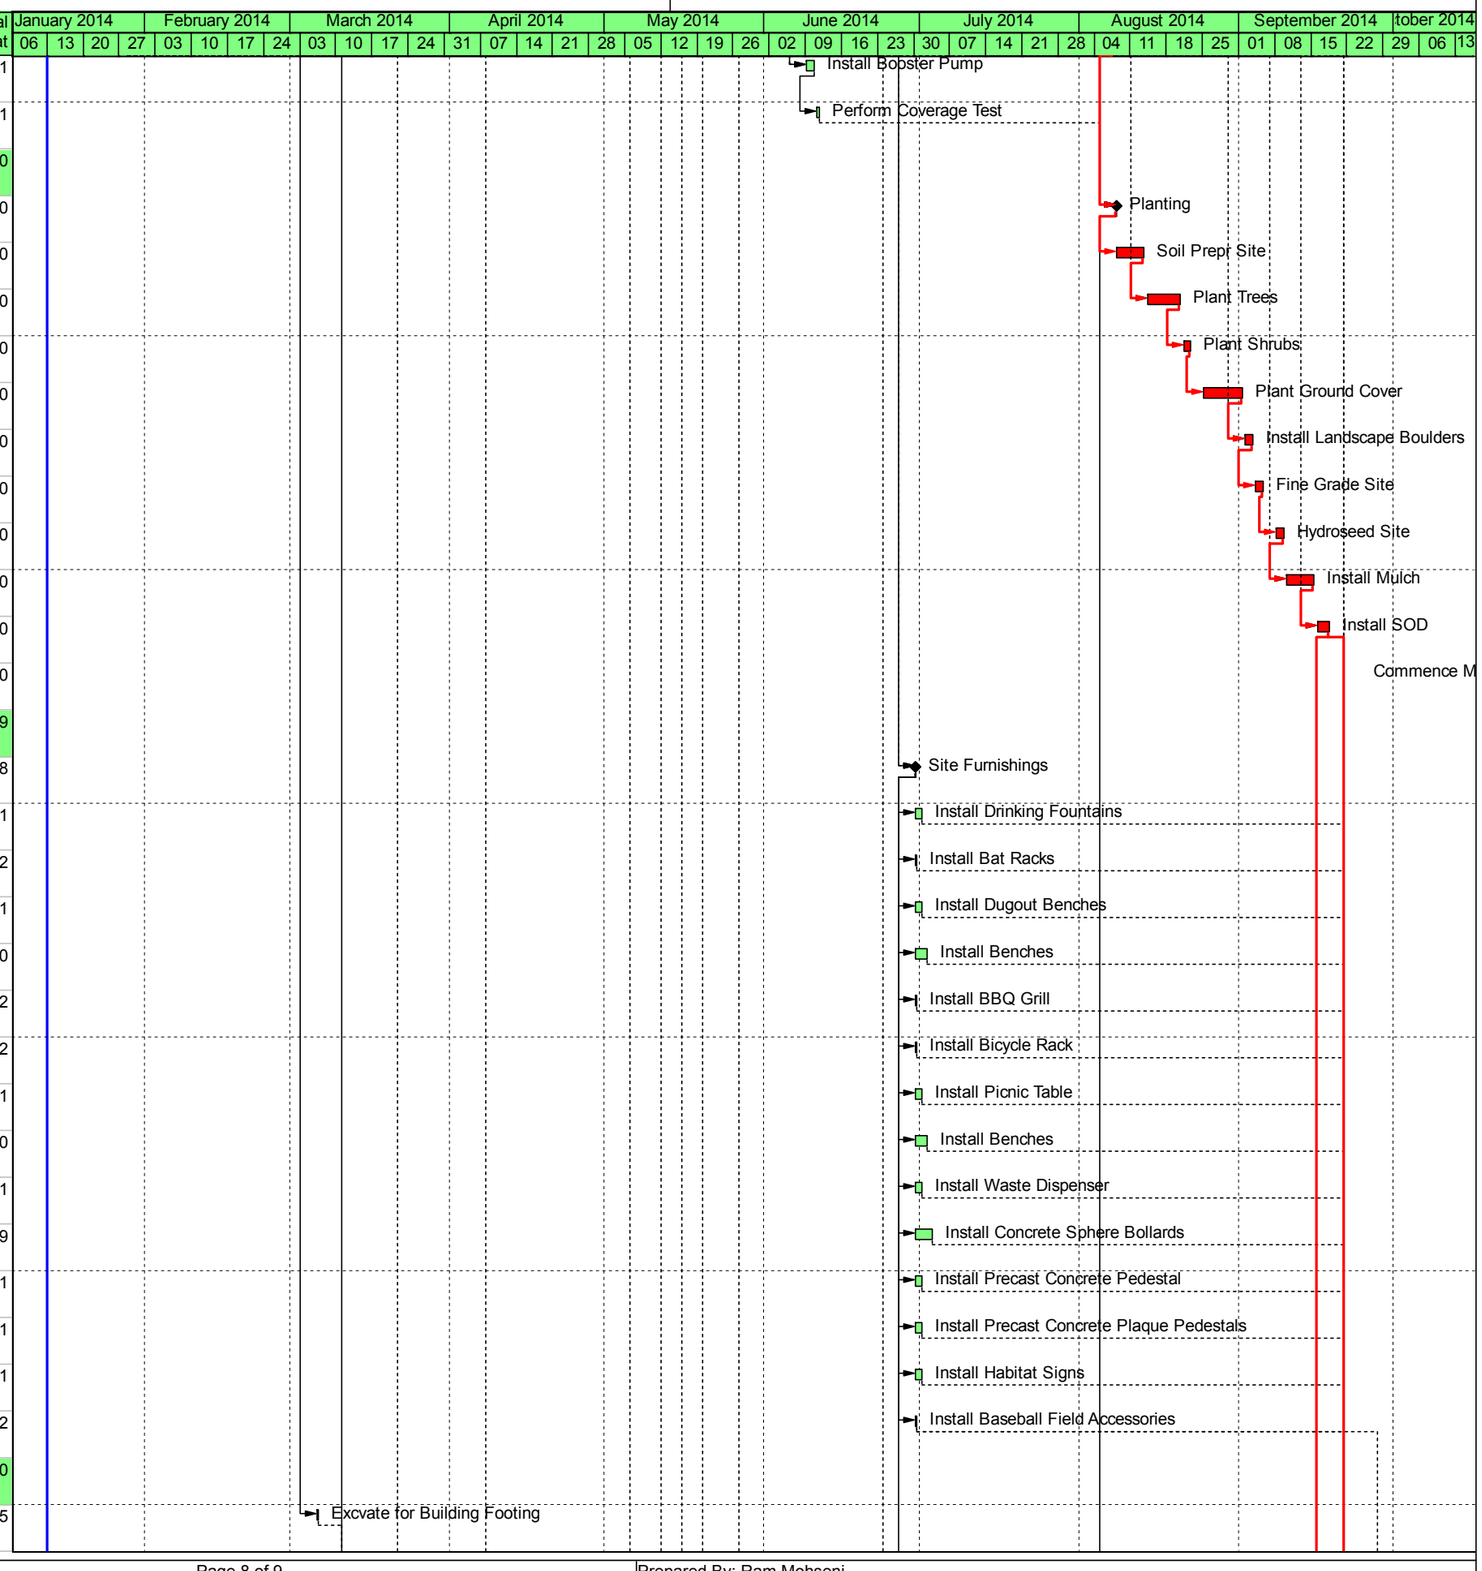

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Prepared By: Ram Mohseni

© Primavera Systems, Inc.

Activity ID	Activity Name	Original	Start	Finish	Actual Start	Actual Finish	Total Float
2370	Install Underground Plumbing	2	14-Mar-14	17-Mar-14			60
2380	Install Underground Electrical	2	18-Mar-14	19-Mar-14			60
2390	Install Footings for Masonary Walls	3	20-Mar-14	24-Mar-14			60
2400	Install Masonary Walls/ Door Frames	10	25-Mar-14	07-Apr-14			60
2410	Install Concrete Slab	3	08-Apr-14	10-Apr-14			60
2420	Install Rough Carpentry/ Trellis Beams	10	11-Apr-14	24-Apr-14			60
2430	Install Rough Plumbing	5	25-Apr-14	01-May-14			60
2440	Install Rough Electrical	5	02-May-14	08-May-14			60
2450	Install Metal Decking	4	09-May-14	14-May-14			60
2460	Install Roofing	2	15-May-14	16-May-14			60
2470	Install Doors	2	19-May-14	20-May-14			60
2480	Install Mesh Screen Panels	2	21-May-14	22-May-14			60
2490	Install Wood Paneling	5	23-May-14	29-May-14			60
2500	Install Tile	10	30-May-14	12-Jun-14			60
2510	Install Finish Electrical	5	13-Jun-14	19-Jun-14			60
2520	Install Finish Plumbing	5	20-Jun-14	26-Jun-14			60
2530	Install Partitions	2	27-Jun-14	30-Jun-14			60
2540	Install Accessories	2	01-Jul-14	02-Jul-14			60
HOA Improvement		63	30-Jun-14	24-Sep-14			0
1180	HOA Improvement	0	30-Jun-14				58
2550	Install Irrigation	5	30-Jun-14	04-Jul-14			58
2560	Plant Shrubs	1	08-Aug-14	08-Aug-14			33
2565	Punch List/ Closeout	3	19-Sep-14	23-Sep-14			0
2566	Demobilization	1	24-Sep-14	24-Sep-14			0
2570	Completion Date	0		24-Sep-14			0

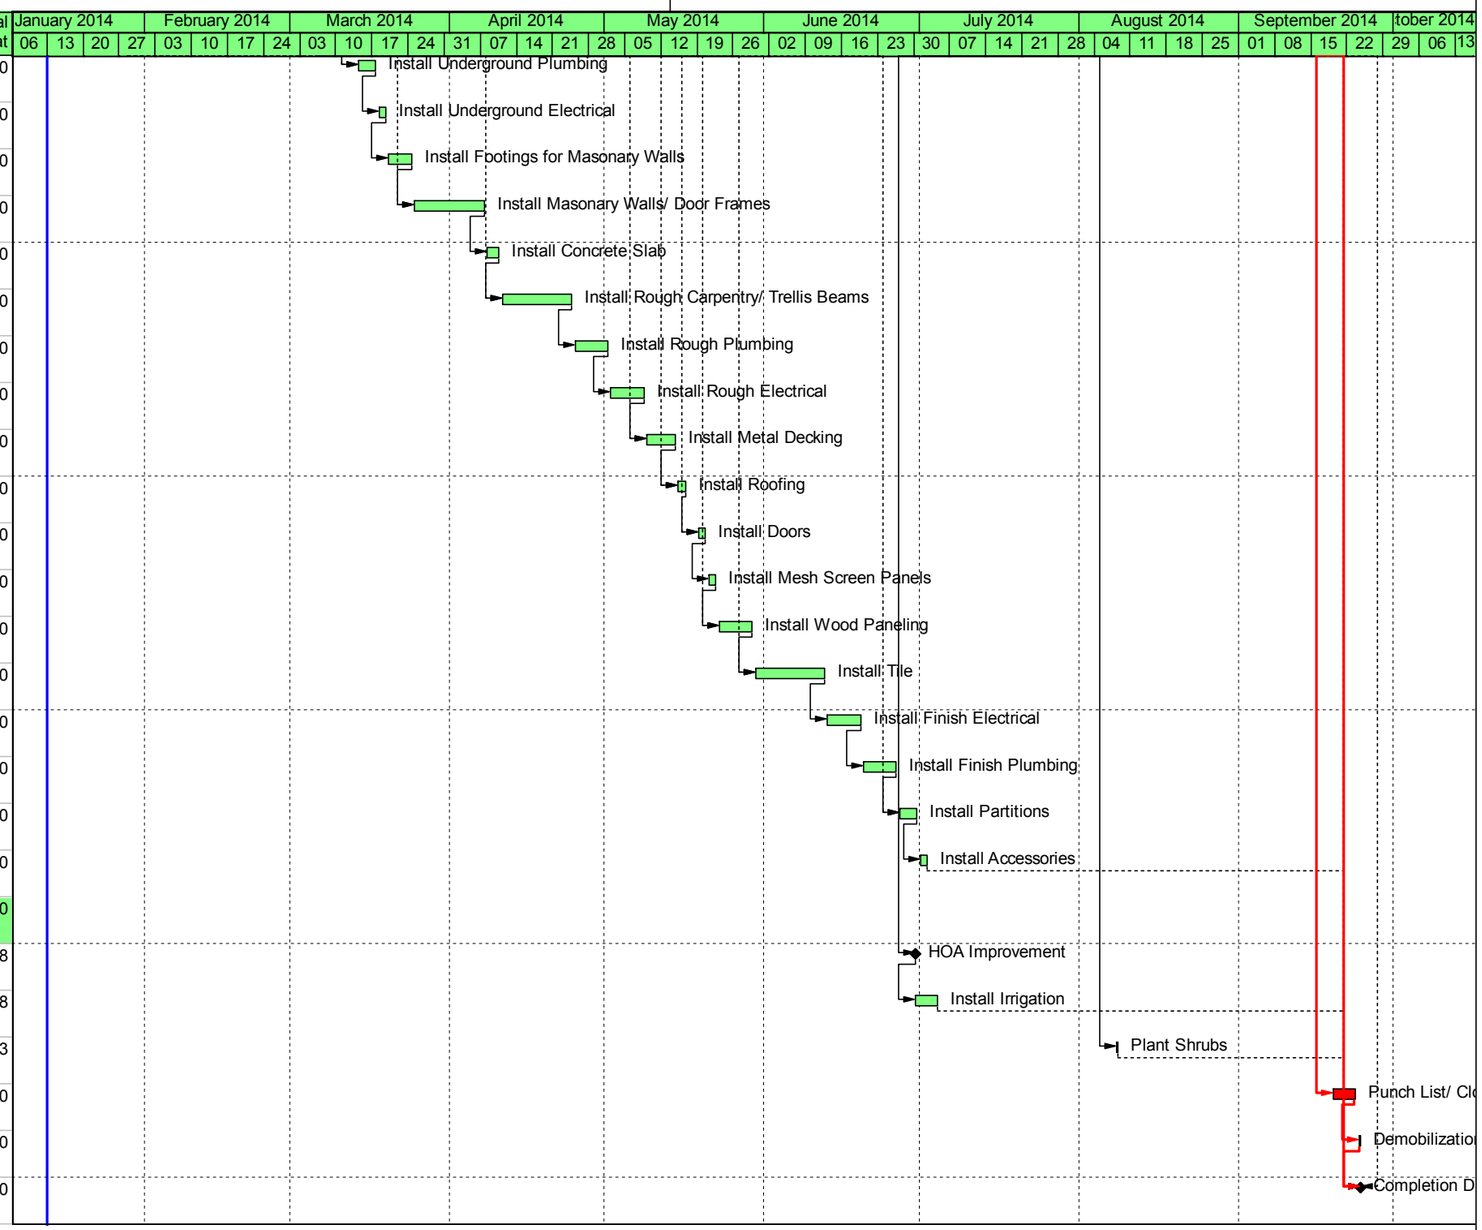

© Primavera Systems, Inc.
